

**BASIC DESIGN STUDY REPORT**  
**ON**  
**THE PROJECT FOR SECONDARY SCHOOL**  
**TEACHER TRAINING FACILITY IMPROVEMENT**  
**AT DOMASI COLLEGE OF EDUCATION**  
**IN**  
**THE REPUBLIC OF MALAWI**

**AUGUST, 2003**

**JAPAN INTERNATIONAL COOPERATION AGENCY (JICA)**  
**KUME SEKKEI CO., LTD.**

**G R 1**

**JR**

**03-204**

**BASIC DESIGN STUDY REPORT**  
**ON**  
**THE PROJECT FOR SECONDARY SCHOOL**  
**TEACHER TRAINING FACILITY IMPROVEMENT**  
**AT DOMASI COLLEGE OF EDUCATION**  
**IN**  
**THE REPUBLIC OF MALAWI**

**AUGUST, 2003**

**JAPAN INTERNATIONAL COOPERATION AGENCY (JICA)**  
**KUME SEKKEI CO., LTD.**

## PREFACE

In response to a request from the Government of the Republic of Malawi, the Government of Japan decided to conduct a basic design study on the Project for Secondary School Teacher Training Facility Improvement at Domasi College of Education and entrusted the study to the Japan International Cooperation Agency (JICA).


JICA sent to Malawi a study team from February 1 to March 3, 2003.

The team held discussions with the officials concerned of the Government of Malawi, and conducted a field study at the study area. After the team returned to Japan, further studies were made. Then, a mission was sent to Malawi in order to discuss a draft basic design, and as this result, the present report was finalized.

I hope that this report will contribute to the promotion of the project and to the enhancement of friendly relations between our two countries.

I wish to express my sincere appreciation to the officials concerned of the Government of Malawi for their close cooperation extended to the teams.

August, 2003



---

Takao Kawakami  
President  
Japan International Cooperation Agency

August, 2003


### Letter of Transmittal

We are pleased to submit to you the basic design study report on the Project for Secondary School Teacher Training Facility Improvement at Domasi College of Education in the Republic of Malawi.

This study was conducted by Kume Sekkei Co., Ltd., under a contract to JICA, during the period from January 2003 to August 2003. In conducting the study, we have examined the feasibility and rationale of the project with due consideration to the present situation of Malawi and formulated the most appropriate basic design for the project under Japan's grant aid scheme.




Finally, we hope that this report will contribute to further promotion of the project.

Very truly yours,




Hiroyuki Tsuchiya  
Project Manager,  
Basic Design Study Team on  
The Project for Secondary School  
Teacher Training Facility Improvement  
at Domasi College of Education.  
Kume Sekkei Co., Ltd.

# MAP OF MALAWI

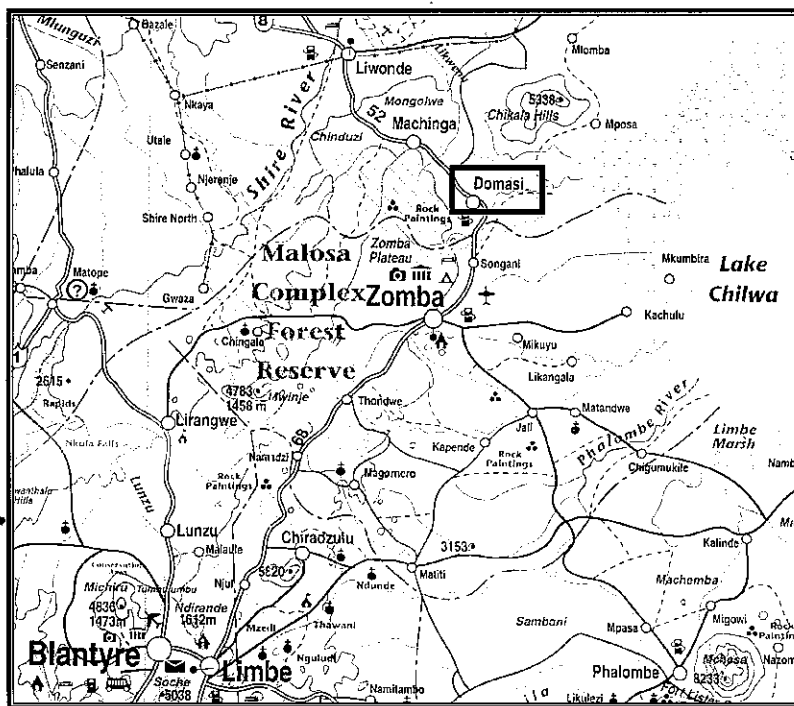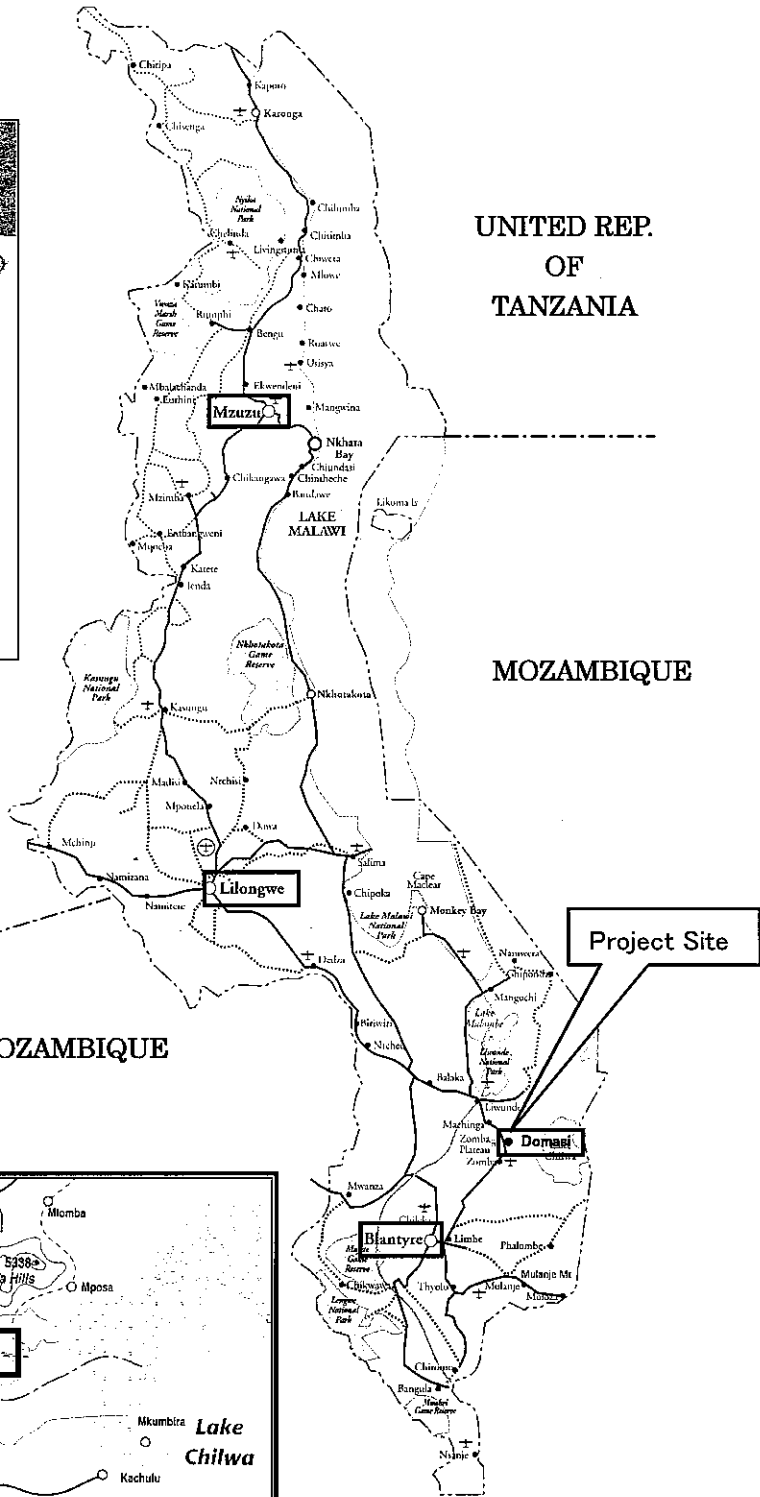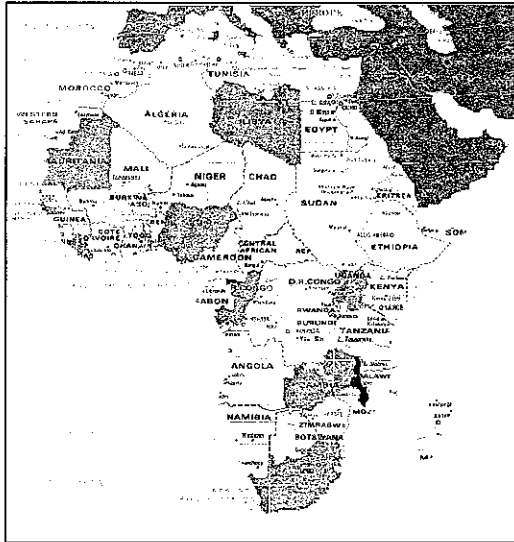

# MAP OF DOMASI AREA





DEMONSTRATION SECONDARY SCHOOL



GYMNASIUM



CORRIDOR

THE PROJECT FOR SECONDARY SCHOOL TEACHER TRAINING FACILITY IMPROVEMENT AT DOMASI COLLEGE OF EDUCATION IN THE REPUBLIC OF MALAWI

## LIST OF ABBREVIATION

CDSS	Community Day Secondary Schools
CERT	Centre for Educational Research and Training
CIDA	Canadian International Development Agency
CONGOMA	Council for Non-Governmental Organizations in Malawi
DCE	Domasi College of Education
DCSS	District Conventional Secondary School
DDLGA	Department of District and Local Government Administration
DEO	District Education Office
DfID	Department for International Development
DSS	Day Secondary School
DVEO	Divisional Education Office
EDMU	Education Development Management Unit
EFA	Education for All
EMIS	Education Management Information System
F	Form
FPE	Free Primary Education
GABLE	Girls Attainment in Basic Literacy and Education
IHSP	Integrated Household Survey on Poverty
INSET	In-Service Secondary Education Teacher Training Programme
JCE	Junior Certificate Examination
MANEB	Malawi National Examination Board
MASAF	Malawi Social Action Fund
MASAFII	Malawi Second Social Action Fund
MASTEP	Malawi Special Teacher Education Programme
MIE	Malawi Institute of Education
MIITEP	Malawi Integrated In-service Teacher Education Programme
MK	Malawi Kwacha
MNCU	Malawi National Commission for UNESCO
MNLS	Malawi National Library Service
MoEST	Ministry of Education Science and Technology
MoESC	Ministry of Education Sports and Culture
MoF	Ministry of Finance
MoHP	Ministry of Health and Population
MoTW	Ministry of Transport and Works
MPRSP	Malawi Poverty Reduction Strategy Paper
MSCE	Malawi School Certificate Examinations
MTEF	Medium Term Expenditure Framework
NCSS	National Conventional Secondary School
NDP	National Decentralization Program
PIF	Policy & Investment Framework
PIU	Project Implementation Unit
PRSP	Poverty Reduction Strategy Paper
PSLCE	Primary School Leaving Certificate Examination
SADC	Southern African Development Cooperation
SBS	Southern African Building Standard
SMASSE	The Strengthening of Mathematics and Science Education in Secondary School Project
SSTEP	Secondary School Teacher Education Project
STD	Standard
TDC	Teacher Development Centre
TDU	Teacher Development Unit
TED	Teacher Education
TTC	Teacher Training College
TTIS	Teacher Training Institutions
UNICEF	United Nations Children Education Fund



## List of Figures & Tables

### List of Figures

Fig. No.	Title
Figure 1-1	Semester at DCE
Figure 2-1	Weather Condition in Zomba (2000)
Figure 2-2	Organization of demonstration secondary school
Figure 2-3	Water distribution plan by the Domasi Water Supply Project
Figure 2-4	Layout plan of the planned facilities
Figure 2-5	Study plan of demonstration secondary school
Figure 2-6	Study plan of staff house
Figure 2-7	Study plan of female hostel
Figure 2-8	Study plan of computer room
Figure 2-9	Study plan of gymnasium
Figure 2-10	Layout plan of Ordinary Classroom
Figure 2-11	Layout plan of laboratories
Figure 2-12	Layout plan of handicrafts and HE workshops
Figure 2-13	Layout plan of administration rooms
Figure 2-14	Layout plan of multipurpose hall
Figure 2-15	Section plan of demonstration secondary school
Figure 2-16	Section plan of gymnasium
Figure 2-17	Flowchart of water supply
Figure 2-18	Flowchart of Sewerage
Figure 2-19	Calculation method of numbers of sanitary fixtures
Figure 2-20	Project implementation flow

### List of Tables

Table No.	Title
Table 1-1	Three Faculties of DCE
Table 1-2	Number of Students in 2002: (Total 492, Total Capacity 540)
Table 1-3	Number of Students by Each Form
Table 1-4	Number of Graduates
Table 1-5	Positions of academic and administrative staff members and filled positions and vacancies
Table 1-6	Teacher Training Plan at DCE (2002 ~ 2010)
Table 1-7	Contents of the Request
Table 2-1	Additional request during the field survey
Table 2-2	Primary schools within catchments area
Table 2-3	Number of students subject to enrollment
Table 2-4	Number of secondary school and students within area of demonstration secondary school
Table 2-5	Necessary rooms for the demonstration secondary school
Table 2-6	Activities at multi-purpose hall of secondary school
Table 2-7	Minimum required number of staff house based on the Minimum Requirement by MoEST
Table 2-8	Non boarding conventional secondary school in the south eastern division
Table 2-9	Number of female applicants for aptitude test and number of those passing the test
Table 2-10	Weekly schedule of use for the computer room
Table 2-11	Existing computers at DCE
Table 2-12	Weekly schedule of use for the gymnasium



<b>Table No.</b>	<b>Title</b>
Table 2-13	The results of the field survey on existing boreholes near DCE
Table 2-14	Water consumption before and after the project
Table 2-15	Contents of the requested equipment
Table 2-16	Equipment required to implement the curriculum
Table 2-17	Minimum range of equipment required for use of facilities
Table 2-18	Minimum range of equipment required for school operation
Table 2-19	Secondary school facilities based on MoEST standards (with World Bank assistance)
Table 2-20	Comparison of room sizes of various secondary education facilities
Table 2-21	Examination of facility size
Table 2-22	Examination of bedroom size for female hostels
Table 2-23	Ground survey results
Table 2-24	Main structure and Design loads
Table 2-25	Construction materials to be used
Table 2-26	Planned water consumption of each new facility per day
Table 2-27	Result of water quality test
Table 2-28	Calculation of electrical power consumption
Table 2-29	Outline of electric service line extension work
Table 2-30	Power system for trunk and branch circuit
Table 2-31	Planned luminous intensity for main rooms
Table 2-32	Planned facility equipment be
Table 2-33	Comparison between local and selected method for the project
Table 2-34	Finishing plan for exterior
Table 2-35	Finishing plan for interior
Table 2-36	Examination of curriculum and equipment
Table 2-37	List of planned main equipment
Table 2-38	List of planned furniture
Table 2-39	Mortar Mixing Table (cement: sand)
Table 2-40	Quality Control Plan
Table 2-41	Procurement of material
Table 2-42	Project Implementation Schedule
Table 2-43	Support Staff of DCE
Table 2-44	Recurrent Cost of DCE
Table 2-45	Running Cost (Public Utility Cost) of DCE
Table 2-46	Monthly Utility Cost paid by DCE in 2002
Table 2-47	Maintenance Cost paid by DCE
Table 2-48	Price List of DCE Services (from September 01, 2002)
Table 2-49	Maintenance Staff of DCE
Table 2-50	Outlines of Building Periodic Inspections
Table 2-51	Lives of Major Building Service Equipment
Table 2-52	Outline of Required Equipment Maintenance
Table 2-53	Trial Calculation of Operating/Maintenance Expenses (Mk / year)
Table 2-54	Trial Estimation of Electric Charge
Table 2-55	Water Supply Volume for Planned Facilities
Table 2-56	Trial Calculation of Water Charge fro Planned Facilities
Table 3-1	Effects of and Degree of Improvement by Project Implementation
