


F - 162

The Study on Storm Water Drainage Plan for the Colombo Metropolitan Region in the Democratic Socialist Republic of Sri Lanka
JAPAN INTERNATIONAL COOPERATION AGENCY

Figure 21.1
Overall Construction Schedule

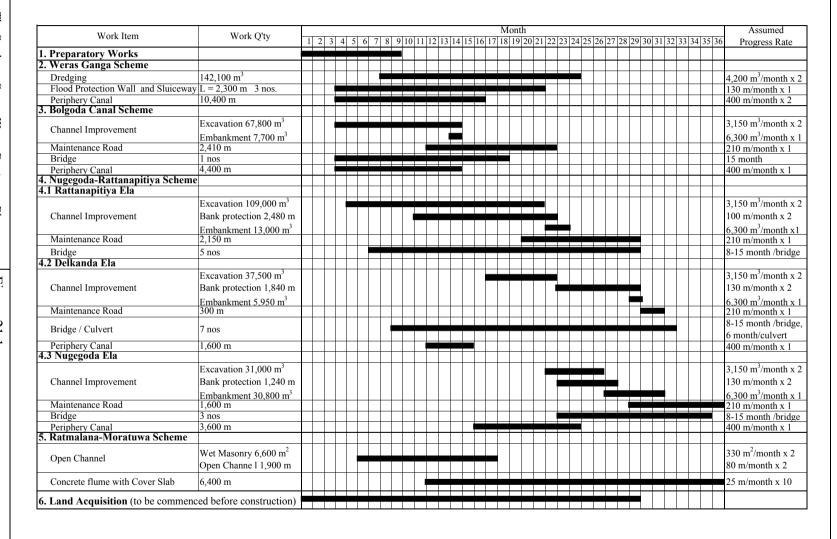

The Study on Storm Water Drainage Plan
for the Colombo Metropolitan Region
in the Democratic Socialist Republic of Sri Lanka
JAPAN INTERNATIONAL COOPERATION AGENCY

| Figure 23.1 | Proposed Project Implementation Schedule

2004 2005 2006 2007 2008 2009 Item 4 6 8 10 12 2 4 6 8 10 12 2 4 6 8 10 12 4 6 8 10 12 2 4 6 8 10 12 2 4 6 8 10 12 0. Funding for the Project Procurement of Consulting Services 1.1 Selection of Consultants 1.2 Detailed Field Survey and Investigation 1.3 Basic Design/Detailed Design 1.4 Preparation of Tender Documents 1.5 Detailed Environmental Survey and Approval Clearance 1.6 Assistance for Prequalification, Tender and Contract 1.7 Construction Supervision 2. Main Civil Works 2.1 Prequalification for Tender 2.2 Tender and Contract 2.3 Preparatory Works 2.4 Weras Ganga Scheme 2.5 Bolgoda Canal Scheme 2.6 Nugegoda-Rattanapitiya Scheme 2.7 Ratmalana-Moratuwa Scheme 2.8 Construction of Resettlement Site (Area Grading) . Procurement of O&M Equipment 3.1 Prequalification for Tender 3.2 Tender and Contract 3.3 Manufacturing and Delivery . Land Acquisition 4.1 Structure Sites 4.2 Storm Water Retention Area (Proposal)
